

1	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1	-	Initiation	7 days	Thu 27-02-25	Sun 09-03-25	
2	-	Define project scope	3 days	Thu 27-02-25	Mon 03-03-25	
3	-	Assign team roles	1 day	Tue 04-03-25	Tue 04-03-25	2
4	-	Secure budget approv	1 day	Wed 05-03-25	Wed 05-03-25	3
5	-5	Stakeholder meeting	1 day	Thu 06-03-25	Thu 06-03-25	4
6	-	Charter approval	1 day	Sun 09-03-25	Sun 09-03-25	5
7	-	Planning	8 days	Mon 10-03-25	Wed 19-03-25	1
8	-	Create WBS	2 days	Mon 10-03-25	Tue 11-03-25	6
9	-	Develop schedule	2 days	Wed 12-03-25	Thu 13-03-25	8
10	-5	Risk assessment	2 days	Sun 16-03-25	Mon 17-03-25	9
11	-5	Resource allocation	1 day	Tue 18-03-25	Tue 18-03-25	10
12	-	Tool setup (Figma/Git	1 day	Wed 19-03-25	Wed 19-03-25	11
13	-	Execution	35 days	Thu 20-03-25	Wed 07-05-25	7
14	-	UI Design	10 days	Thu 20-03-25	Wed 02-04-25	7
15	-	Homepage design	1 day	Thu 20-03-25	Thu 20-03-25	12
16	-	Login page design	1 day	Sun 23-03-25	Sun 23-03-25	15
17	-	Signup page design	1 day	Mon 24-03-25	Mon 24-03-25	16
18	-5	Freelancer dashboard design	1 day	Tue 25-03-25	Tue 25-03-25	17
19	-9	Category navigation design	1 day	Wed 26-03-25	Wed 26-03-25	18
		Task		Inactive Task	Start-only	Е
		Split		Inactive Milestone $\Diamond$	Finish-only	3

	External Milestone	<b>♦</b>	Manual Summary			
	External Tasks		Manual Summary Rollup			
	Project Summary		Duration-only		Manual Progress	
Date: Mon 05-05-25	Summary		Manual Task		Progress	
Project: msproj11	Milestone	<b>♦</b>	Inactive Summary		Deadline	$\hat{\mathbf{T}}$
	Split		Inactive Milestone	$\Diamond$	Finish-only	3
	Task		Inactive Task		Start-only	С


D	0	Task Mode	Task Name	Duration	Start	Finish	Predecessors
20		-5	Booking page desig	1 day	Thu 27-03-25	Thu 27-03-25	19
21		4	Review system desi	-	Sun 30-03-25	Sun 30-03-25	20
22		-9	Payment mockup design	1 day	Mon 31-03-25	Mon 31-03-25	21
23		4	Filtering UI design	1 day	Tue 01-04-25	Tue 01-04-25	22
24		-5	Responsive design testing	1 day	Wed 02-04-25	Wed 02-04-25	23
25		-9	Development	25 days	Thu 03-04-25	Wed 07-05-25	14
26		-9	Set up React environment	1 day	Thu 03-04-25	Thu 03-04-25	
27	00	-	Implement homepag	1 day	Mon 07-04-25	Mon 07-04-25	26
28		-5	Create login component	1 day	Tue 08-04-25	Tue 08-04-25	27
29		-5	Build signup form	1 day	Wed 09-04-25	Wed 09-04-25	28
30		-5	Develop category navigation	1 day	Thu 10-04-25	Thu 10-04-25	29
31		-9	Freelancer card component	1 day	Mon 14-04-25	Mon 14-04-25	30
32		-	Booking button syst	t1 day	Tue 15-04-25	Tue 15-04-25	31
33		-5	Review section UI	1 day	Wed 16-04-25	Wed 16-04-25	32
34		-5	Payment mockup pa	1 day	Thu 17-04-25	Thu 17-04-25	33
			Task		Inactive Task	Start-only	Е
			Split		Inactive Milestone		3




D	0	Task Mode	Task Name	Duration	Start	Finish	Predecessors
35			Price sorting feature	1 day	Mon 21-04-25	Mon 21-04-25	34
36		-9	Rating display component	1 day	Tue 22-04-25	Tue 22-04-25	35
37			Search bar functiona	1 day	Wed 23-04-25	Wed 23-04-25	36
38		-9	User profile dropdown menu	1 day	Thu 24-04-25	Thu 24-04-25	37
39		-9	Service availability toggle	1 day	Mon 28-04-25	Mon 28-04-25	38
40		-9	Booking confirmation modal	1 day	Tue 29-04-25	Tue 29-04-25	39
41		-9	Responsive mobile menu	1 day	Wed 30-04-25	Wed 30-04-25	40
42		-5	Error message templates	1 day	Thu 01-05-25	Thu 01-05-25	41
43		-9	Freelancer portfolio gallery	1 day	Mon 05-05-25	Mon 05-05-25	42
44	00		Price range slider fil	1 day	Tue 06-05-25	Tue 06-05-25	43
45		-5	FAQ accordion sect	1 day	Wed 07-05-25	Wed 07-05-25	44
46		-9	<b>Monitoring/Control</b>	6 days	Thu 08-05-25	Thu 15-05-25	25,13
47		-5	Weekly progress review	1 day	Thu 08-05-25	Thu 08-05-25	45
48		-5	Bug tracking	1 day	Mon 12-05-25	Mon 12-05-25	47
			Task		Inactive Task	Start-only	Е
			Split		Inactive Milestone	Finish-only	3
			Milestone	<b>♦</b>	Inactive Summary	Deadline	Ŷ



D	0	Task Mode	Task Name	Duration	Start	Finish	Predecessors
49		-5	Budget check	1 day	Tue 13-05-25	Tue 13-05-25	48
50		-5	UI validation	1 day	Wed 14-05-25	Wed 14-05-25	49
51		-5	Client feedback	1 day	Thu 15-05-25	Thu 15-05-25	50
52		-5	Closing	5 days	Sun 18-05-25	Thu 22-05-25	46
53		-5	Final documentation	1 day	Sun 18-05-25	Sun 18-05-25	51
54		-5	Lessons learned	1 day	Mon 19-05-25	Mon 19-05-25	53
55		-5	Project presentation	1 day	Tue 20-05-25	Tue 20-05-25	54
56		-5	Sponsor approval	1 day	Wed 21-05-25	Wed 21-05-25	55
57		-5	Archive files	1 day	Thu 22-05-25	Thu 22-05-25	56



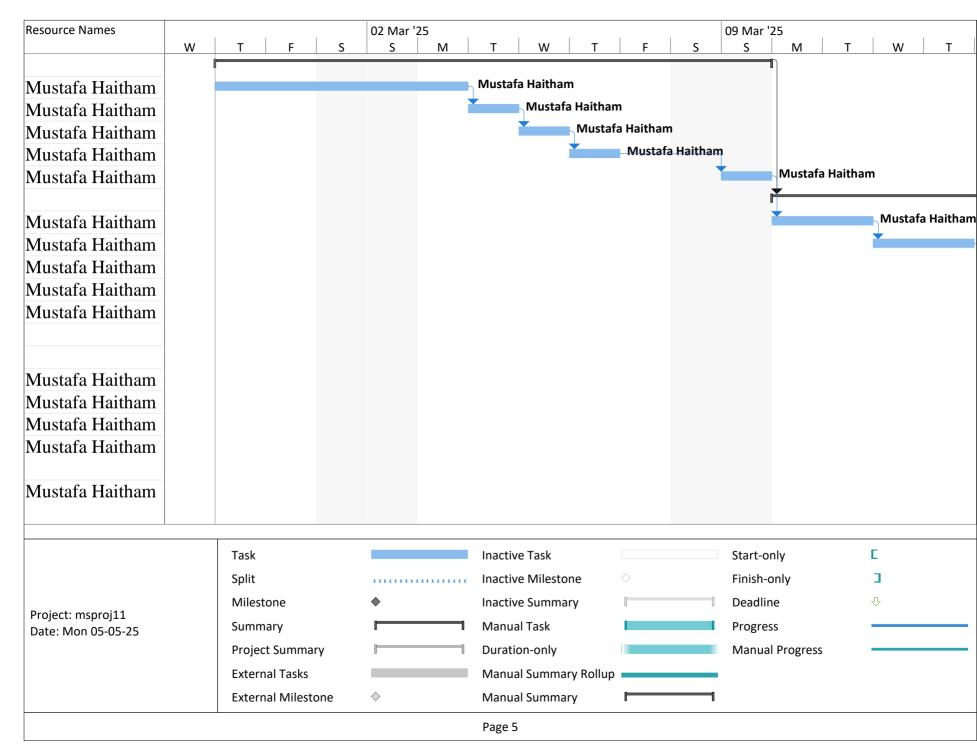

Resource Names					02 Mar '	25								09 Mar	'25			
	W	Т	F	S	S	M		Т	W	-	Γ	F	S	S	M	Т	W	Т
Mustafa Haitham																		
Mustafa Haitham																		
Mustafa Haitham																		
Mustafa Haitham																		
Mustafa Haitham																		
Parez																		
Parez																		
Parez																		
Parez																		
Parez																		
Parez																		
Parez																		
Parez																		
Parez																		
		Task					l	nactiv	e Task					Start-c	only		Е	
		Split					1	nactiv	e Milest	one		$\Diamond$		Finish-	only		3	
Dunington and 144		Milesto	one		<b>♦</b>		I	nactiv	e Summ	ary				Deadli	ne		$\hat{\mathbf{T}}$	
Project: msproj11 Date: Mon 05-05-25		Summa	ary					Manua	ıl Task					Progre	SS			
		Project	Summa	ry			<b>—</b> [	Duratio	on-only					Manua	al Progre	SS		
		Externa	al Tasks				ı	Manua	ıl Summ	ary Ro	llup							
		Extern	al Milest	one	$\Diamond$		ſ	Manua	ıl Summ	ary			1					
							ı	Page 6										

Resource Names				02 Mar '	25							09 Mar	'25			
	W	T F	S	S	М	Т	W	Т		F	S	S	М	Т	W	Т
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
Parez																
		Task				Inact	ive Task					Start-o	only		С	
		Split				Inact	ive Milest	tone	<			Finish-	only		3	
Drainati marzaitt		Milestone		<b>♦</b>		Inact	ive Summ	nary				Deadli	ne		Ŷ	
Project: msproj11 Date: Mon 05-05-25		Summary				l Man	ual Task		ı			Progre	SS			
		Project Summai	ſy			Dura	tion-only					Manua	al Progre	SS		
		External Tasks				Man	ual Summ	ary Rol	lup =			I				
		External Milesto	one	$\Diamond$		Man	ual Summ	ary	ľ							
						Page	7									

							Mar '2										09 Mar			1	,		
_	W	T	F	:	S		S	M		Т	<u> </u>	W	Т		F	S	S	IV	1	Т		W	Т
Parez																							
Parez																							
Parez																							
Mustafa Haitham																							
Mustafa Haitham																							
Mustafa Haitham																							
Mustafa Haitham																							
Mustafa Haitham																							 
		Task				_				Inacti							Start-c				Е		
		Task Split								Inacti	ve Mil	ilestor		□			Start-c Finish-				=	]	
Project: msproi11						•					ve Mil	ilestor		→				only				]	
Project: msproj11 Date: Mon 05-05-25		Split								Inacti	ve Mil ve Sur	ilestor mmar		□			Finish-	only ne			=	]	
		Split Milest	nary	nmary	у				 ¬	Inacti Inacti	ve Mil ve Sur ıal Tas	ilestor mmar sk		• • • • • • • • • • • • • • • • • • •			Finish- Deadli	only ne ess	gress		=	]	
		Split Milest Summ	nary ct Sum		y					Inactiv Inactiv Manu Durat	ve Mil ve Sur ial Tas ion-or	ilestor mmar sk nly					Finish- Deadli Progre	only ne ess	gress		=	]	

Page 8

